


Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Hyperlocal Courier Dispatch & Tracking Engine (Problem Statement #23)


SRN: PES1UG24AM377 | Section: G | Jira Project: Mathin (Key: SCRUM)

Deliverable 1 — Jira Backlog with Epics and User Stories

The Backlog view with the Epic panel expanded, showing all 6 Epics derived from the Lab 1 functional and non-functional requirements. Each Epic's green progress bar reflects that all child User Stories were carried through to completion across the two simulated sprints.

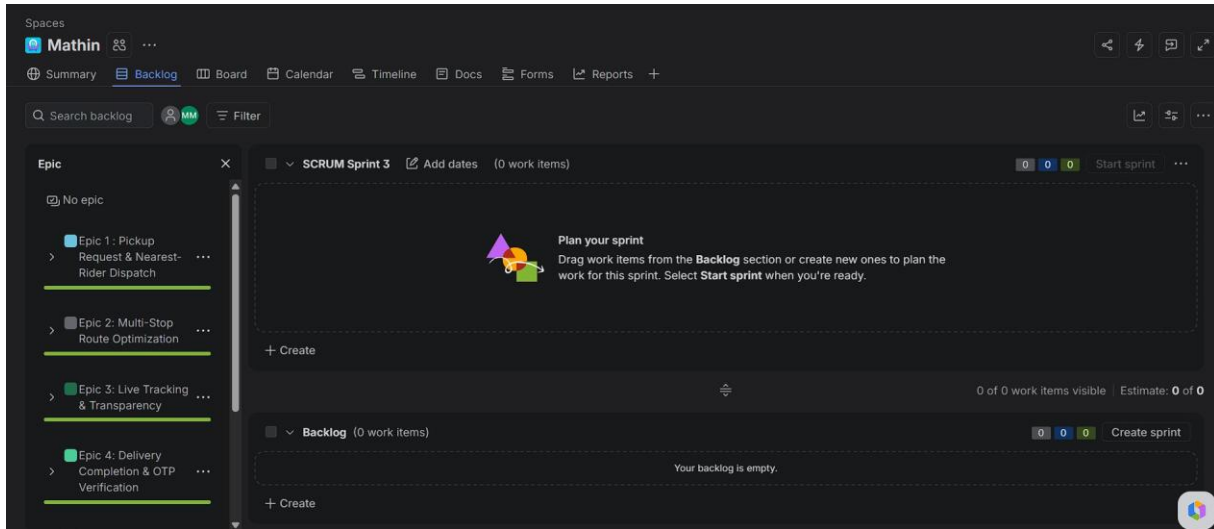


Epic panel — Epics 1–4 (Pickup Request & Dispatch, Route Optimization, Live Tracking, OTP Verification)

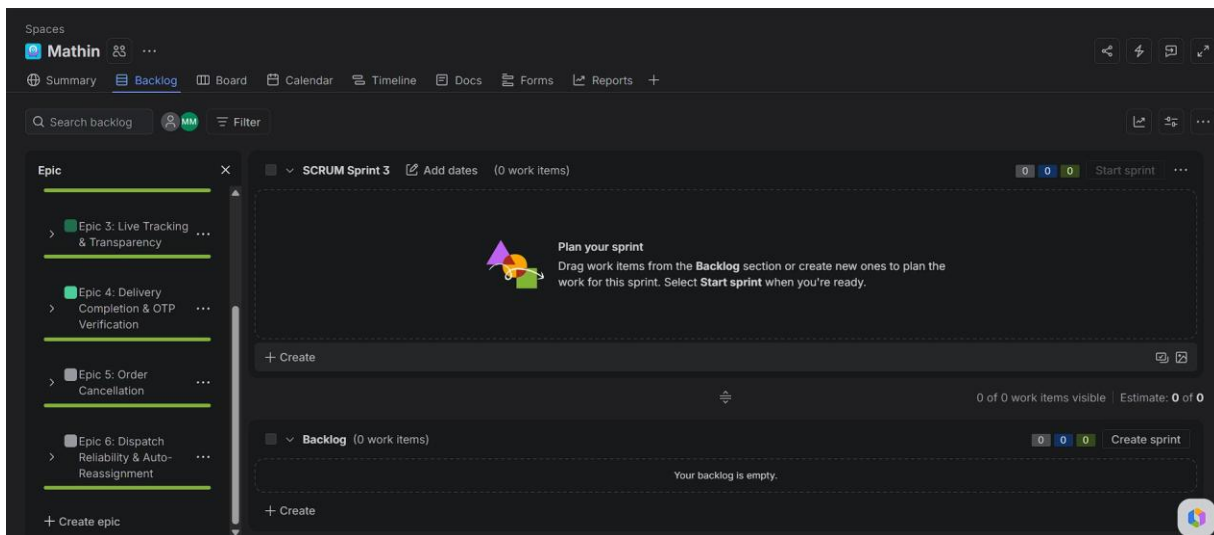

Epic panel — Epics 3–6 (scrolled view, showing Order Cancellation and Dispatch Reliability & Auto-Reassignment)

Deliverable 2 — Sprint Burndown Chart

Burndown data for Sprint 2 (September 1–8, 2026), covering 5 user stories totaling 35 story points. The Remaining Work line (red) drops from 35 to 0 almost immediately relative to the Guideline (grey ideal burn rate), since for this simulation all stories were moved through To Do → In Progress → Done within an 8-minute window (2:40pm–2:48pm) rather than across the full week.

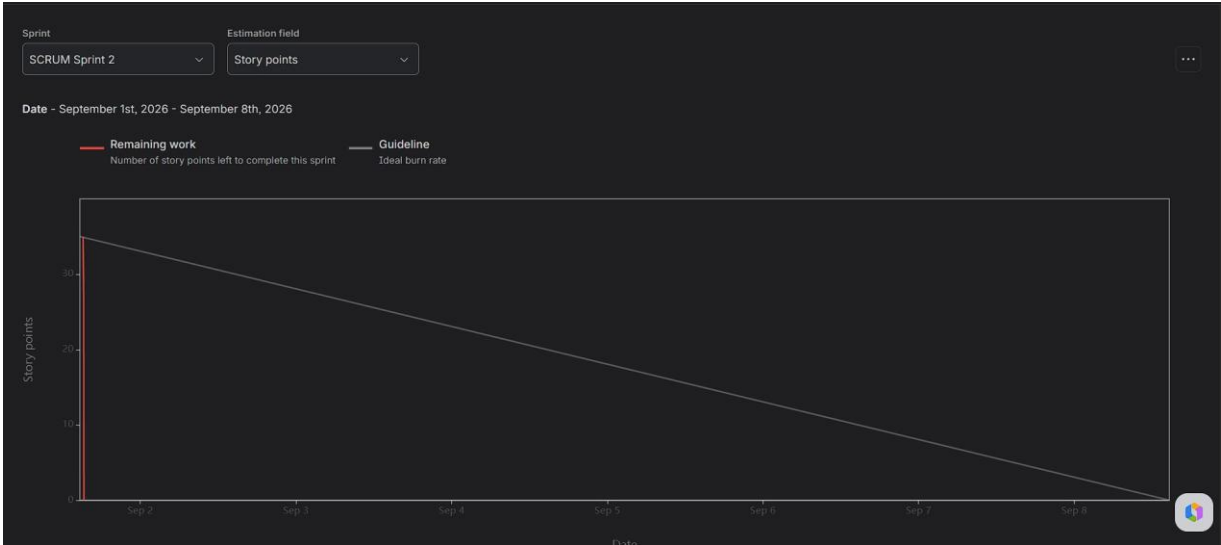

Sprint 2 burndown chart: Remaining Work vs. Guideline, Sep 1–8, 2026

Completed work items							View in All work navigator
Key	Summary	Work type	Epic	Status	Assignee	Story points	
SCRUM-13	Story 2.1: Optimize Stop Sequence	Story	Epic 2: Multi-Stop ...	Done		8	
SCRUM-15	Story 3.2: Low-Latency Telemetry	Story	Epic 3: Live Trackl...	Done		13	
SCRUM-17	Story 4.2: Handle OTP Mismatch	Story	Epic 4: Delivery Co...	Done		3	
SCRUM-19	Story 6.1: Auto-Reassign Unaccepted Orders	Story	Epic 6: Dispatch R...	Done		8	
SCRUM-18	Story 5.1: Cancel Before Pickup	Story	Epic 5: Order Canc...	Done		3	
Work items completed outside of sprint							
Key	Summary	Work type	Epic	Status	Assignee	Story points	

Completed work items table — all 5 stories marked Done, story points summing to 35

Reflection Questions

1. Did your estimations reflect the actual effort?

Since this was a simulation sprint (stories went from one status to another in minutes and not actual time for development), the story points represent planned relative effort rather than actual relative effort. In a real-world setting, stories with the greatest uncertainty in this backlog – Story 3.2 (Low-Latency Telemetry, 13 points) and the 8-point stories (Nearest Rider Matching, Optimize Stop Sequence, Auto-Reassign Unaccepted Orders) – would be those stories where estimation drift is most likely to occur..

2. Was your backlog well-prioritized?

Yes. All the core flow stories (Request Pickup, Nearest Rider Matching, See Rider Location, Enter OTP for Delivery, Automatic Reassignment of Unaccepted Orders) had High priority because the courier dispatch app cannot function without a proper request dispatch tracking and confirmation flow. The secondary and edge case stories (Optimize Stop Sequence, OTP Mismatch, Cancel Before Pickup) had Medium priority because the product still works without them in an initial release..

3. How did your simulated sprint align with your plan?

The stories with the highest priority and lowest uncertainty, totaling 4 stories (18 points), were done in Sprint 1 to ensure we had the end-to-end flow in place before anything else. Sprint 2 was assigned the rest of the stories (5 stories, 35 points) including the story with the highest uncertainty (Low-Latency Telemetry, 13 points). The sprints were done completely with the event log for Sprint 2 indicating that all 5 stories were completed in a span of 8 minutes. In a one-week sprint, 35 points would not be manageable by one individual..

4. What insights did the burndown chart give about your team's capacity?

In Sprint 2's burndown chart, there is a dramatic decrease in the Remaining Work line from 35 to 0 story points almost vertically, much faster than expected according to the Guideline. The assumption in the Guideline is that of the linear nature of the burn-down process throughout the entire week. In a real sprint, this would have served as an indicator to look into; either the stories were underestimated, or, more likely in this case, all work was done within a sudden rush without a realistic distribution. This emphasizes the importance of the Guideline as an indicator: the burn-down should happen steadily and incrementally..
